

FRH Healthcare App


Phased design and delivery schedule for the mobile application redesign — 24 screens across four release phases, from onboarding through the booking and consultation flow.

PREPARED FOR	FRH
ISSUED	23 September 2026
PROJECT START	7 September 2026
TARGET COMPLETION	8 October 2026

SCREENS DELIVERED	IN PROGRESS	REMAINING	WORKING DAYS LEFT
4 of 24	7 screens	13 screens	12 days
Onboarding & authentication	Core app experience · due 28 Sep	Across Phases 2 and 3	23 Sep to 8 Oct, including today

01 Visual Timeline

Five calendar weeks, 7 September to 11 October 2026. Bars show design working time; diamonds mark client delivery dates. Shaded columns are weekends and are excluded from all working-day counts.

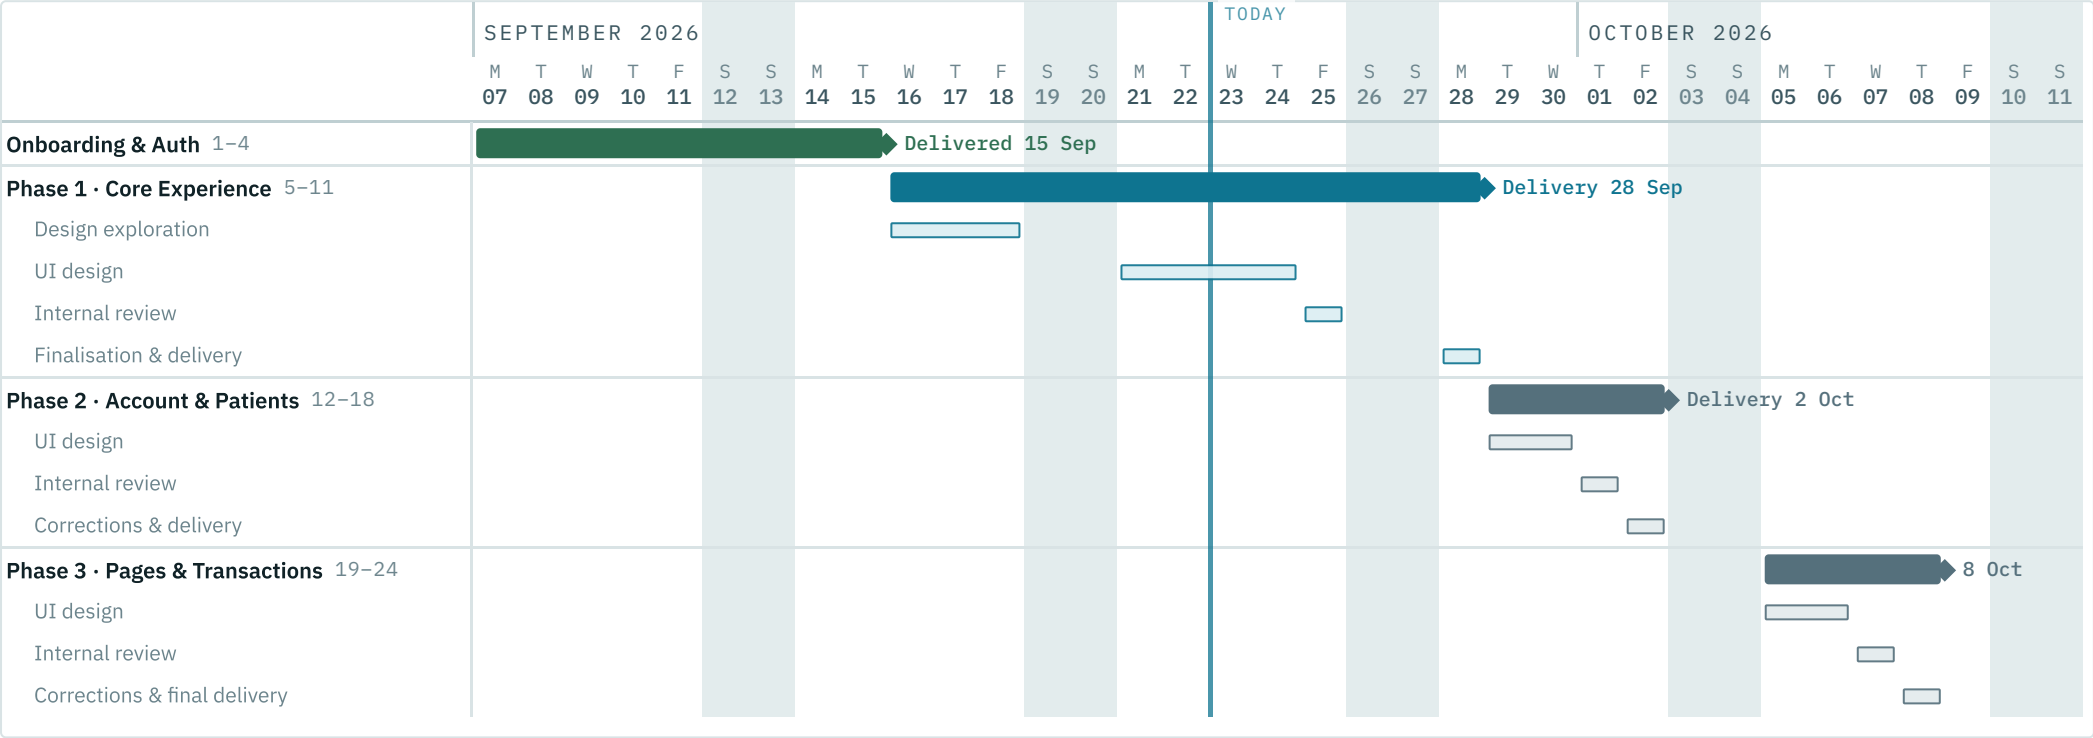

02 Phase Schedule

All durations are working days, Monday to Friday. Delivery dates assume feedback and approvals are received within the buffers described in Section 05.

PHASE	SCREENS COVERED	START DATE	END DATE	DURATION	STATUS
Onboarding & Authentication Screens 1-4	Welcome / Intro, Loading Screen, Register, Login	7 Sep 2026	15 Sep 2026	7 working days	COMPLETED
Phase 1 — Core App Experience Screens 5-11	Homepage, Chat with Doctor Information, Chat Screen, Other Services, Service Detail, Book Now, Bookings	16 Sep 2026	28 Sep 2026	9 working days	IN PROGRESS
Phase 2 — User Account & Patient Management Screens 12-18	Notifications, My Profile, Edit My Profile, Addresses, Saved Patients, Add Patient Details, Reports	29 Sep 2026	2 Oct 2026	4 working days	SCHEDULED
Phase 3 — Additional Pages & Transaction Flow Screens 19-24	About Us, Help, FAQ, Payment Loading, Video Consultancy, Booking Flow (Select Patient · Choose Location & Schedule · Verify Information), plus logout confirmation popup and Terms & Conditions	5 Oct 2026	8 Oct 2026	4 working days	SCHEDULED
Full project	24 screens & supporting components	7 Sep 2026	8 Oct 2026	24 working days	

03 Screen Inventory

DELIVERED · 15 SEP 2026 Onboarding & Authentication 1. Welcome / Intro Page 2. Loading Screen 3. Register Page 4. Login Page	PHASE 1 · DUE 28 SEP 2026 Core App Experience 5. Homepage 6. Chat with Doctor Information Page 7. Chat Screen 8. Other Services Page 9. Service Detail Page 10. Book Now Page 11. Bookings Page	PHASE 2 · DUE 2 OCT 2026 User Account & Patient Management 12. Notifications 13. My Profile 14. Edit My Profile 15. Addresses 16. Saved Patients 17. Add Patient Details 18. Reports	PHASE 3 · DUE 8 OCT 2026 Additional Pages & Transaction Flow 19. About Us 20. Help 21. FAQ 22. Payment Loading Page 23. Video Consultancy 24. Booking Flow Select Patient Choose Location & Schedule Verify Information Additional components Logout confirmation popup · Terms & Conditions page
--	---	--	--

04 Status Notes

COMPLETED WORK The onboarding and authentication flow (Screens 1–4) ran from 7 September and was delivered on 15 September 2026 — seven working days. This covers Welcome / Intro, Loading, Register and Login — establishing the visual language, type scale, colour system and component patterns carried through every later phase. No further work is scheduled on these screens unless changes are requested.	UPCOMING MILESTONES 28 Sep 2026 — Phase 1, Core App Experience (7 screens). The next major milestone. 2 Oct 2026 — Phase 2, User Account & Patient Management (7 screens), four working days after Phase 1. 8 Oct 2026 — Phase 3, Additional Pages & Transaction Flow (6 screens, including the three-step booking flow, plus two supporting components), four working days after Phase 2.	ASSUMPTIONS & DEPENDENCIES Phases run sequentially; each start date depends on the previous phase being delivered on schedule. Durations count working days only — Monday to Friday, excluding public holidays. Content, branding assets and any required API or service details are assumed to be available at the start of each phase. Screen counts and scope are as listed in Section 03. The schedule covers UI/UX design only; development and QA are outside this timeline.
--	--	--

05 Timeline Conditions

REVIEW & FEEDBACK BUFFER

Each phase includes dedicated time for internal quality checks, client review, minor corrections and design refinements. These are built into the durations shown above rather than added on top of them.

ADDITIONAL CHANGES

“Any major changes, additional screens, new requirements, or heavy design revisions requested after approval may require additional time and will be estimated separately based on the scope of changes.”

CLIENT DEPENDENCY

“Timeline may vary depending on the speed of feedback, approvals, and requirement clarifications from the client side.”
